
**DAVIS SQUARE ARCHITECTS**  
 240A Elm St.  
 Somerville, MA 02144  
 617.628.5700  
 www.davis-square-architects.com

---

Project: NEW CONSTRUCTION OF  
 32 MARION STREET SENIOR HOUSING  
 32 MARION STREET, BROOKLINE, MA 02446


Title: DEMOLITION PLAN

Checked by:	1:840/0 No.
Designed by:	
Drawn by:	
Author:	
Project No.:	2020064.00
Scale:	As Indicated
Date:	11/23/22

D100

A-1 DEMOLITION PLAN  
 3/32" = 1'-0"

ID	i	WBS	Task Mode	Task Name	Duration	Start	Finish	Aug '23				Sep '23				Oct '23	
								23	30	6	13	20	27	3	10	17	24
1		1	→	<b>Demo</b>	<b>36 days</b>	<b>Mon 8/14/23</b>	<b>Mon 10/2/23</b>										
2	📅	1.1	→	Demo 4-5	2 days	Mon 8/14/23	Tue 8/15/23										
3	📅	1.2	→	Foundation Removal of Buidling 4-5	4 days	Wed 8/16/23	Mon 8/21/23										
4		1.3	→	Remove Slab 4-5	2 days	Tue 8/22/23	Wed 8/23/23										
5		1.4	→	Demo 1-2-3	12 days	Wed 8/16/23	Thu 8/31/23										
6		1.5	→	Foundation Removal of Buildings 1-2-3	6 days	Fri 9/1/23	Fri 9/8/23										
7		1.6	→	Remove slab 1-2-3	3 days	Mon 9/11/23	Wed 9/13/23										
8		1.7	→	Demo 6	4 days	Fri 9/1/23	Wed 9/6/23										
9		1.8	→	Foundation Removal of Building 6	4 days	Thu 9/7/23	Tue 9/12/23										
10	📅	1.9	→	Remove Slab 6	2 days	Wed 9/13/23	Thu 9/14/23										
11		1.10	→	Demo 7	6 days	Thu 9/7/23	Thu 9/14/23										
12		1.11	→	Foundation Removal of Buidling 7	6 days	Fri 9/15/23	Fri 9/22/23										
13		1.12	→	Remove slab 7	3 days	Mon 9/25/23	Wed 9/27/23										
14		1.13	→	Demobilize/Clean site	3 days	Thu 9/28/23	Mon 10/2/23										

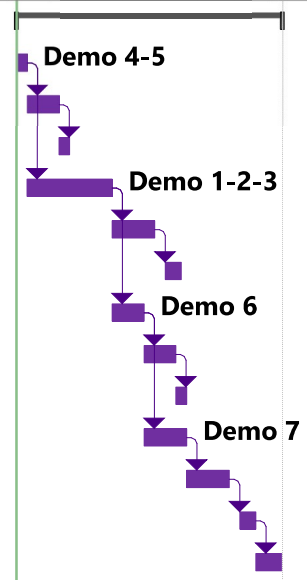

Project: 32 Marion Street - 3 W  
Date: Mon 8/14/23

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
